



ENTSOOG Capacity

Network Code on Capacity Allocation

Frank Roessler
Subject Manager

CAM NC Kick-Off meeting – 9th February 2011

Purpose of General Project Plan

1. Planning the twelve months


- Describe the timely steps, milestones and deliverables
- Stakeholder interaction (SJWSs and consultations)

2. Market engagement


- Engage stakeholders throughout the whole process
- Use today to foster interaction with market parties
- Users to commit to the process

ENTSOEG Capacity Work Group

Internal organisation of the work

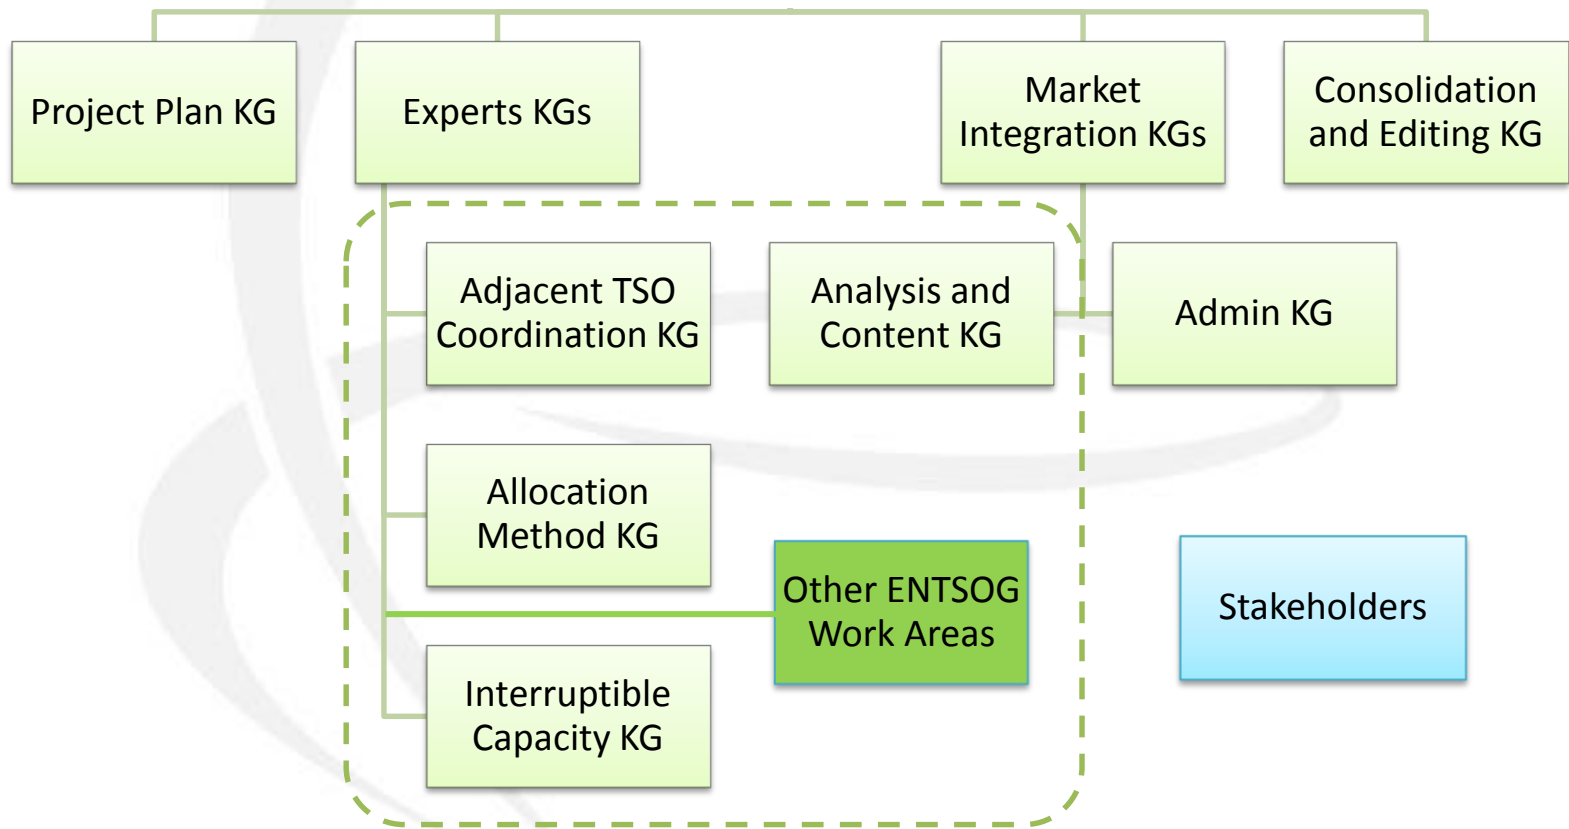

NC Development Process

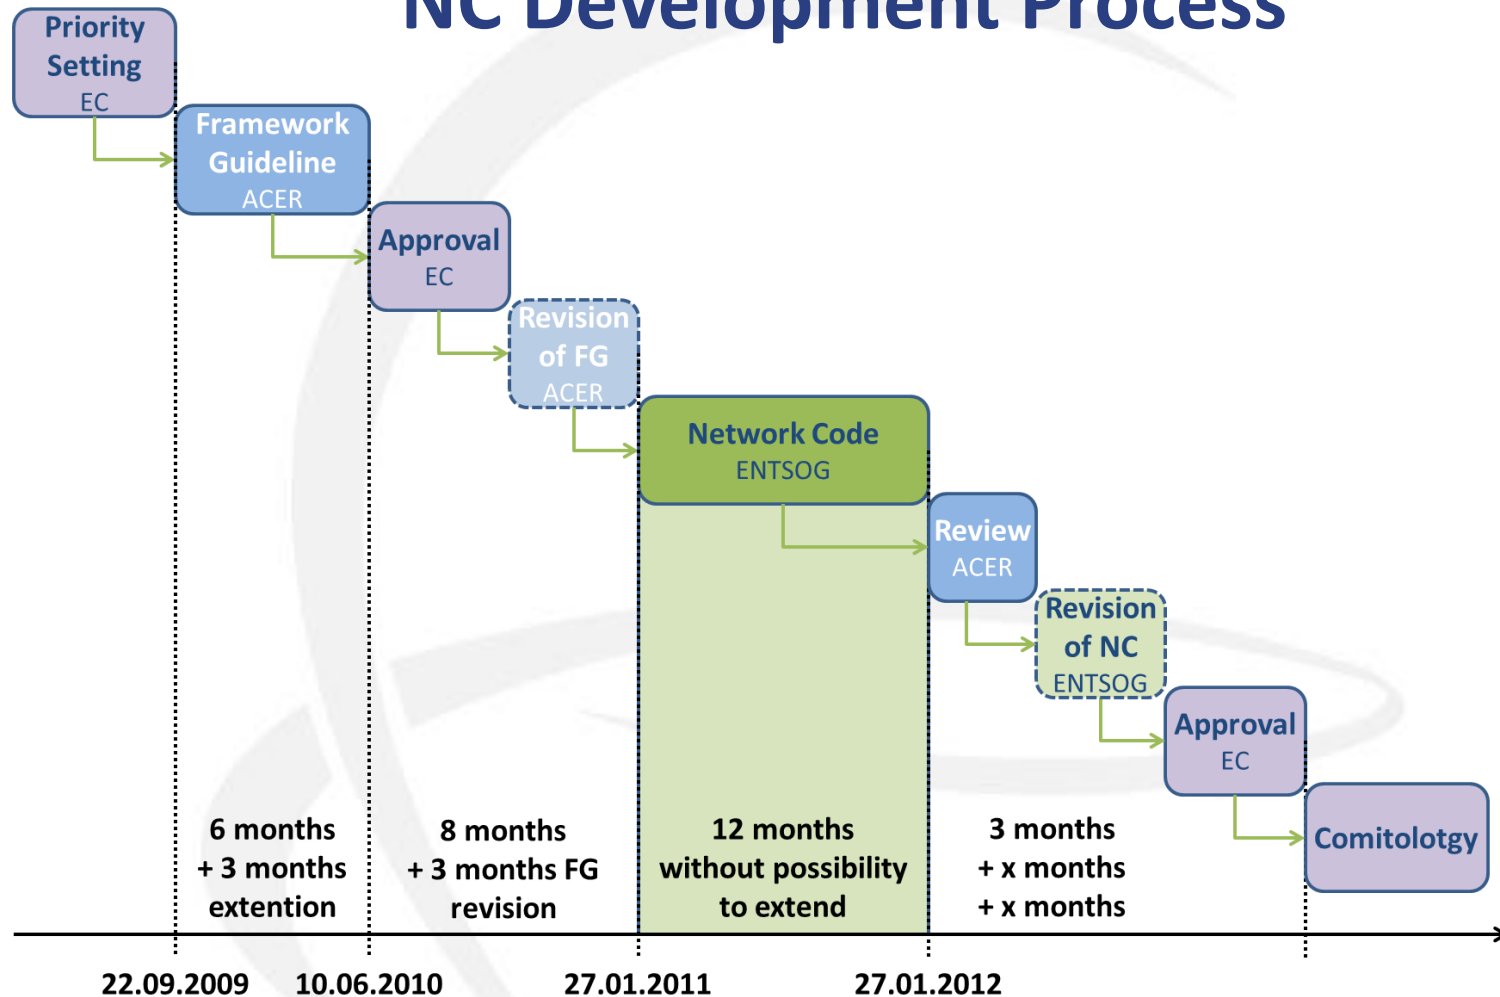

ENTSOG and the market need to manage the time constraints

Key Deliverables

Project Management

- Draft Project Plan

Launch Documentation

- Final Project Plan to be refined after consultation including initial considerations of the pilot CAM network code

SJWS & Bilateral meetings with Stakeholders


- For each SJWS: invitation, agenda, supporting material and minutes
- Bilateral and group meeting material as agreed between the parties

Network Code

- Draft version submitted for consultation by the market
- Consultation Responses Analysis Report
- Final CAM NC approved by ENTSOG for recommendation to ACER


Network Code Engagement Process

Phases of the CAM NC Development

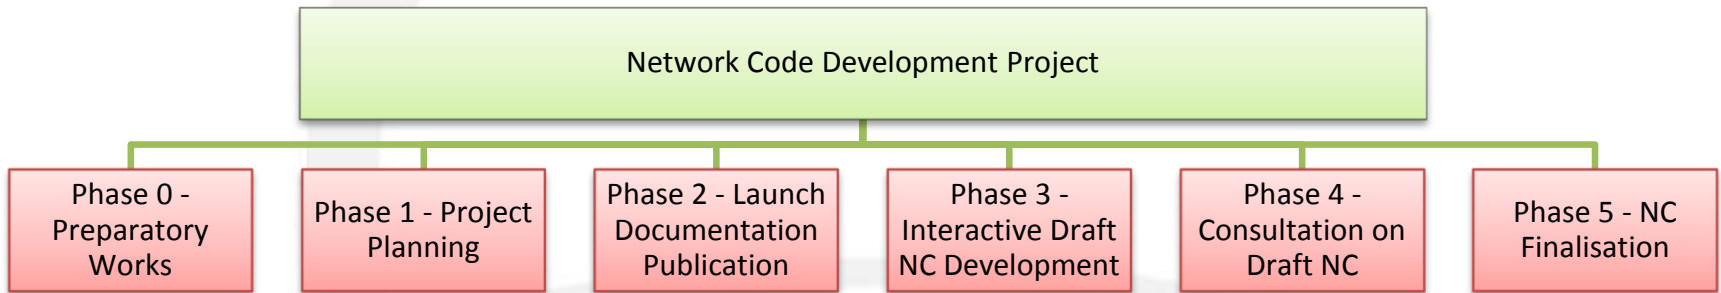

- Detailed internal planning done to underpin the phases
- Uncertainties in the process
 - Parallel entering into force of ACER and new consultation
 - Unknown outcome from debate on Target Model
 - Parallel work on other code areas (balancing, tariffs, interoperability)
 - GRI development
 - Commitments

Project Schedule

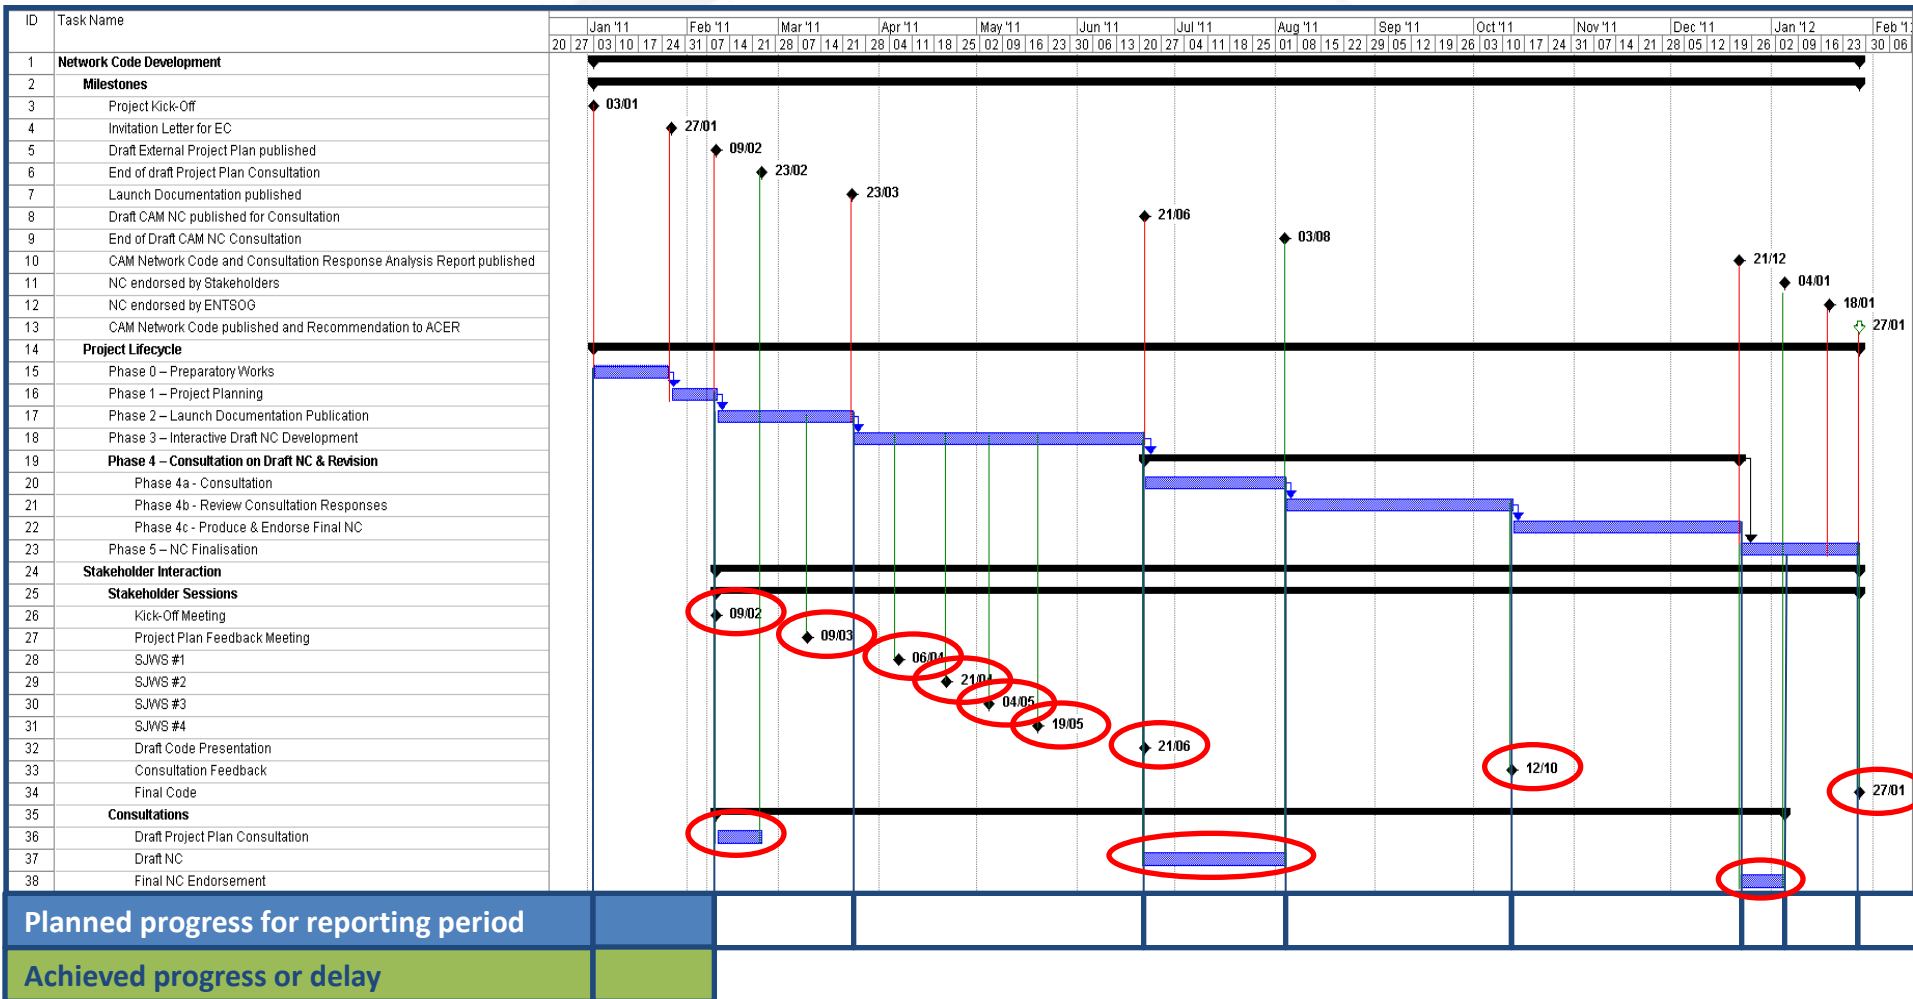

Project Plan Consultation

Consultation on the planning

- **Response form in Appendix of Project Plan**
- **Market to provide view on planned:**
 - Steps
 - Milestones
 - Deliverable
 - Schedule – phases, meetings etc.
 - Stakeholder engagement – consultations and sessions
- **Please provide us with your opinions by the 23rd of February**

Work shop planned to discuss responses on the 9th of March

Project Plan Consultation

Market participant's commitment

- Engagement of the market is critical for the NC development

Level	Description	Comments
1	Prime Mover	Committed to work on a bilateral basis and dedicate a lot of resources to assist formulate and evaluate/refine ideas/proposals for SJWS consideration – commitment to be intensive and involving many days during intensive phases of the network code development
2	Active SJWS Participant	Expected to attend all SJWS and to read and review all material prior to meetings and to be prepared to explore detail within the SJWS – commitment of around 3 days per month during intensive period of activity
3	Consultation Respondent	Will respond to consultations
4	Inactive	Expected not to actively contribute to the development effort or to participate in the formal consultations

Network Code linked Information



Home

About Us

Publications
& Events

Maps & Data

Secure Area

Contact Us

Welcome



Welcome to ENTSOG.

European Gas TSOs working towards the delivery of the single European gas market.

The European Network of Transmission System Operators for Gas (ENTSO) works to promote the completion and functioning of the internal market and cross-border trade for gas and to ensure the optimal management, coordinated operation and sound technical evolution of the European natural gas transmission network.



Network Code linked Information

[Home](#)[About Us](#)[Publications & Events](#)[Maps & Data](#)[Secure Area](#)[Contact Us](#)

ENTSOG > Capacity Co-ordination

[2008](#) [2009](#) [2010](#) **[2011](#)**

In September 2009 the European Commission has officially invited ERGEG to develop a Framework Guideline on Capacity Allocation. ENTSOG is taking the steps towards the drafting of the Network Code on Capacity Allocation by fostering the dialogue between the Users, ERGEG and European Commission.

This website provides relevant information, documents (comprising position papers and consultation material) throughout all processes.

For any further question please contact :

Frank Roessler

frank.roessler@entsog.eu

T +32 (0)2 894 51 07

T +32 (0)2 894 51 01






Olivier Lebois

olivier.lebois@entsog.eu





T +32 (0)2 894 51 05

T +32 (0)2 894 51 01





CAM Network Code Development

- ▶ **ENTSOG CAM NC General Project Plan (GA-00-00)** 9 Feb 2011  expected
- ▶ Commission invitation to draft the CAM NC  27 Jan 2011  0,59 Mb
- ▶ ERGEG final revised Framework Guideline on CAM (E10-GWG-71-03)  7 Dec 2010  0,08 Mb

ENTSOG Position Papers / Reactions / Reports

- ▶ ENTSOG CMP Consultancy proposal (CAP071-10)  23 Nov 2010  0,53 Mb
- ▶ Position Paper on Existing Capacity (CAP0053-10)  10 Aug 2010  0,33 Mb

ENTSOG - Notes and materials of meetings with externals

- ▶ Notes of Meeting with EC, ACER and ERGEG (CAP0094-11)  21 Jan 2011  0,31 Mb
- ▶ Notes of Meeting with EC and ERGEG (CAP0077-10)  9 Nov 2010  0,35 Mb

Thank You for Your Attention

Frank Roessler, Subject Manager
ENTSOG -- European Network of Transmission System Operators for Gas
Rue Ducale 83, B-1000 Brussels

T: + 32 2 894 5107
M: + 32 496 121 684

EML: Frank.Roessler@entsog.eu
WWW: www.entsog.eu

